

PRESALE DATA

PROJECT AREA MAP (STICK ON FORM R6-5400-11)


ACTIVITY CODE HTH	TRI-POSTED-ACTIVE DATE	MANAGEMENT DIRECTION FROM TRI						
TREE CL. M	SPECIES DF/NF WH	SIZE 12.3"	TR/AC 293	BA/AC	VOL/AC 49.1 GR	NET -MBF	MSLTOE	
		DBH			GR			
					NET			
PRE-TREATMENT (STAND CONDITION, DAMAGING AGENTS, GROUND VEGETATION, ETC.) Mixed stand of second-growth Doug-fir, Noble fir, hemlock and silver fir.								
DATA SOURCE cruise DATE 8/13 BY MB, SH								


TREATMENT PLAN	(TREATMENT OBJECTIVE, SILV. PRESCRIP., RECOMMENDED STOCKING LEVEL, LOGGING PLAN, SALE CONTRACT REQUIREMENTS, ETC.) Ground-based yarding on 8 Acres Skyline yarding on 13 Acres Construct 4 landings: 2 @ 1/4 Ac 2 @ 1/8 Ac Total = .75 Ac.	
	Do not subsoil slopes greater than 30%. Location of skid trails used for equipment fueling/servicing shall be approved by FS.	
EST. NET VOLUME TO BE CUT	TREATMENT PLAN COMPLETED DATE 9/13 BY SH	

LAYOUT & CRUISE	INDICATE METHOD USED TO MARK OR DESIGNATE BOUNDARIES AND/OR TREES. INDICATE TYPE OF CRUISE, SAMPLE SIZE, INTENSITY, GRADING, ETC. Harvest unit boundary marked with blue flagging, blue "Boundary Partial Cut" signs and orange paint. LTM - Leave Tree Marking - All merchantable trees are designated for harvest EXCEPT those marked with orange paint on bole and at stump. (Batch #A0998) Sample tree cruise.	
	CRUISE COMPLETED DATE 9/13 BY SH, MB	DESIGNATION COMPLETED DATE 9/13 BY SH, MB
WORK PLANNED ON ACTIVITY DATE	RECORDS FOR: REFOR-TSI DATE	APPRAISAL COMPLETED DATE

R6-2400-90(6/73)

TIMBER HARVEST ACTIVITY RECORD

COMPARTMENT NAME Tower Rock	COMPT. No.	Stand Tag 529170
Quad Name T. 10, 11 N.	Quad Number 29	
RANGE R. 8 E.	SCALE-MILES 0  1/4	
PROJECT NAME PEAK THTN	UNIT No. 39	ACRES 21

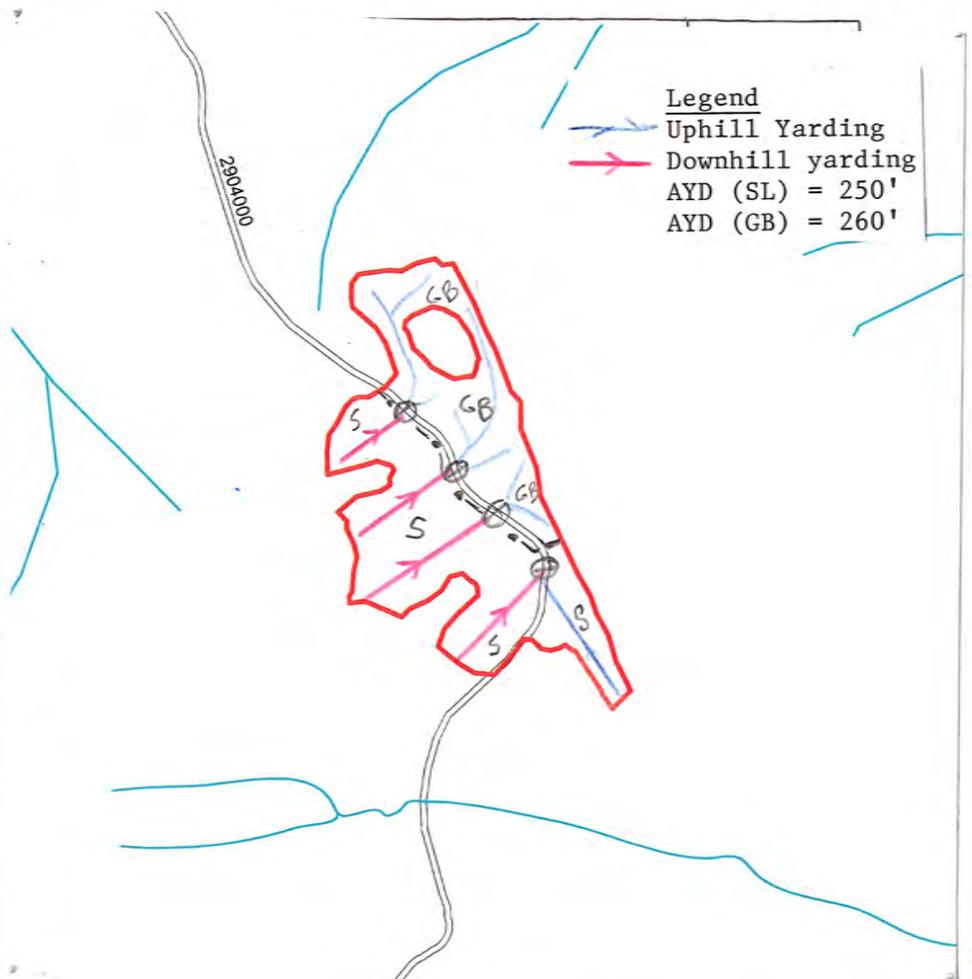

SITE	SLOPE 0-50%	EXPOSURE NE	ELEVATION 3700'
	SOIL	ECOCLASS	SITE INDEX-SITE SPECIES

PRESALE DATA

PROJECT AREA MAP (STICK ON FORM R6-5400-11)

ACTIVITY CODE HTH	TRI-POSTED-ACTIVE DATE	MANAGEMENT DIRECTION FROM TRI						
TREE CL. M	SPECIES DF/NF WH	SIZE 12.3"	TR/AC 143	BA/AC	VOL/AC 24.2 GR	MSLTOE MBF		
		DBH			NET			
					GR			
					NET			
(STAND CONDITION, DAMAGING AGENTS, GROUND VEGETATION, ETC.) Mixed stand of second-growth Doug-fir, hemlock, noble fir, cedar.								
DATA SOURCE Cruise DATE 9/13 BY MB, RR								

(TREATMENT OBJECTIVE, SILV. PRESCRIP., RECOMMENDED STOCKING LEVEL, LOGGING PLAN, SALE CONTRACT REQUIREMENTS, ETC.) Skyline yarding to 2 landings. Construct 8 road-side landings @ 1/8 Ac each. Total = 1.0 Acres.	
Do not subsoil slopes greater than 30%. Location of skid trails used for equipment fueling/servicing shall be approved by FS.	
EST. NET VOLUME TO BE CUT	TREATMENT PLAN COMPLETED DATE 9/13 BY SLH


INDICATE METHOD USED TO MARK OR DESIGNATE BOUNDARIES AND/OR TREES. INDICATE TYPE OF CRUISE, SAMPLE SIZE, INTENSITY, GRADING, ETC. Harvest unit boundary marked with blue flagging, blue "Boundary Partial Cut" signs and orange paint. ITM - Individual Tree Marking - All trees marked with blue paint on bole and at stump designated for harvest. Sample Tree cruise. Orange paint batch #Ac 998, blue #Jo 213.	
CRUISE COMPLETED DATE 9/13 BY MB, RR	DESIGNATION COMPLETED DATE 9/13 BY RR

WORK PLANNED ON ACTIVITY SLASH TREATMENT DATE	RECORDS FOR: REFOR-TSI DATE	APPRAISAL COMPLETED DATE

R6-2400-90(6/73)

TIMBER HARVEST ACTIVITY RECORD

COMPARTMENT NAME Tower Rock	COMPT. No.	Stand Tag 529170
Quad Name T. 10 N.	Quad Number 29	
TWP. R. 8 E.	SCALE-MILES 8 IN. = 1 MILE	
RANGE	UNIT No. 40 ACRES 18	
PROJECT NAME PEAK THIN		

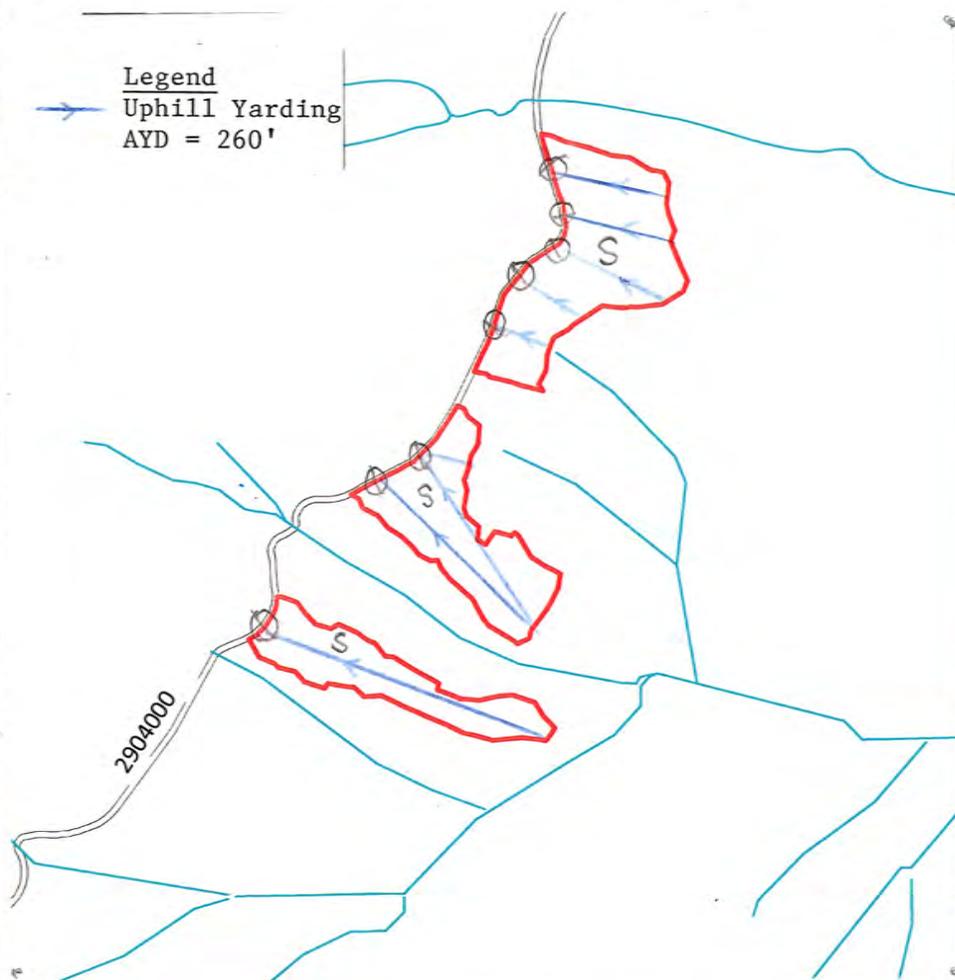

SLOPE 70%	EXPOSURE SE	ELEVATION 3800'
SOIL	ECOCLASS	SITE INDEX-SITE SPECIES

PRESALE DATA

ACTIVITY CODE HTH	TRI-POSTED-ACTIVE DATE	MANAGEMENT DIRECTION FROM TRI					
TREE CL. M	SPECIES DF/WH	SIZE 10.8"	TR/AC 195	BA/AC	VOL/AC 23.1 GR	MSLTOE MBF	
		DBH			NET		
					GR		
					NET		
PRE-TREATMENT (STAND CONDITION, DAMAGING AGENTS, GROUND VEGETATION, ETC.) Second-growth stand comprised of Doug-fir and western hemlock, with scattered red cedar.							
DATA SOURCE 'cruise DATE 9/13 BY MB, RR							

TREATMENT PLAN (TREATMENT OBJECTIVE, SILV. PRESCRIP., RECOMMENDED STOCKING LEVEL, LOGGING PLAN, SALE CONTRACT REQUIREMENTS, ETC.) All ground-based yarding to two landings. Reconstruct 1000' of existing temp. road. → (med. costs) Construct 800' of new temp road (15% side slope) Construct 2 landings @ 1/2 Ac. each. Total = 1.0 Ac Do not subsoil slopes greater than 30%. Location of skid trails used for equipment fueling/servicing shall be approved by FS.	
EST. NET VOLUME TO BE CUT	TREATMENT PLAN COMPLETED DATE 9/13 BY STH

LAYOUT & CRUISE INDICATE METHOD USED TO MARK OR DESIGNATE BOUNDARIES AND/OR TREES. INDICATE TYPE OF CRUISE, SAMPLE SIZE, INTENSITY, GRADING, ETC. Harvest unit boundary marked with blue flagging, blue "Boundary Partial Cut" signs and orange paint. Center trees of "gaps" marked with double bands of pink paint on bole of tree and at stump. Timber to be removed is Designated by Description. (refer to C2.351# in the timber sale contract.) PNT cruise. Orange paint batch #A0998, pink #X0756.	
CRUISE COMPLETED DATE 9/13 BY MB, RR	DESIGNATION COMPLETED DATE 9/13 BY MB, RR

WORK PLANNED ON ACTIVITY RECORDS FOR: SLASH TREATMENT BY DATE	REFOR-TSI DATE	APPRAISAL COMPLETED DATE
R6-2400-90(6/73)		TIMBER HARVEST ACTIVITY RECORD

PROJECT AREA MAP (STICK ON FORM R6-5400-11)

IDENTITY	COMPARTMENT NAME E. Canyon Ridge	COMPT. No.	Stand Tag 539151
	Quad Name	Quad Number 39	
	TWP. T. 10 N.	SCALE-MILES 0 ————— 1	
	RANGE R. 9 E.	NORTH ↑	
PROJECT NAME PEAK THIN	UNIT No. 45	ACRES 45	

